Example of Detailed Schedule of Work

ID	Task Name	Duration	Start	Finish
1				
2	**Planning/Preliminary Phase**			
3	Receipt of Letter of Award			
4	Submission of Work Program			
5	Preparation of Insurance and Performance Bond			
6	Confirmation on Site Measurement			
7	Preparation of Lift Shop Drawing and Lift Material Submission			
8	Lift Shop Drawing Approval and Lift Material Approval by JKR			
9	Submission of 1st Schedule JKKP (Subject to approval from JKKP)			
10	Placement of Equipment Ordering			
11	Equipment Manufacturing			
12	CIDB Levy (Subject to received bill from CIDB)			
13	JKKP Site Registration (Subject to approval from JKKP)			
14	Submission of barricade design and mock up, project signboard drawings, PQP inc. method statement etc.			
15	Submission of CCTV shop drawing and material/catalogue			
16	CCTV shop drawing and material/catalogue approval by JKR			
17	CCTV material delivery on site			
18	Verify Site Condition			
19	Installation of CCTV system (lift lobby)			
20	Equipment Shipping			
21	Customs Clearance, Delivery on Site (Subject to Customs Approval)			
22	**Phase 1: PL1 Block 22 & PL1 Block 23**			
23	Installation of Barricade and secure area			
24	Lift Dismantling			
25	Contruction of Landing door slope (hacking, construct and make good)			
26	Dismantling of existing equipment inside lift shaft such as light fitting, socket outlet and cat ladder			
27	Installation of new lift pit and lift shaft lighting, socket outlet and cat ladder			
28	Installation of Machine Room equipment			
29	Installation of Hoistway equipment			
30	Installation of Landing features			
31	Installation of Car features			
32	Testing & Commissioning			
33	Installation of CCTV system (lift car)			
34	Application of JKKP inspection			
35	Epoxy paint works for lift pit floors and walls			
36	JKKP Inspection (Subject to availability of JKKP inspector)			
37	Lift Phase 1 - Running in period			
38	Making good damages			
39	**Phase 2: PL2 Block 22 & PL2 Block 23**			
40	Installation of Barricade and secure area			
41	Lift Dismantling			
42	Contruction of Landing door slope (hacking, construct and make good)			
43	Dismantling of existing equipment inside lift shaft such as light fitting, socket outlet and cat ladder			
44	Installation of new lift pit and lift shaft lighting, socket outlet and cat ladder			
45	Installation of Machine Room equipment			
46	Installation of Hoistway equipment			
47	Installation of Landing features			
48	Installation of Car features			
49	Testing & Commissioning			
50	Installation of CCTV system (lift car)			
51	Application of JKKP inspection			
52	Epoxy paint works for lift pit floors and walls			
53	JKKP Inspection (Subject to availability of JKKP inspector)			
54	Lift Phase 2 - Running in period			
55	Painting of lift lobby at each floor			
56	Installation of floor signage			
57	Making good damages			
58	**Phase 3: Refurbishment of existing lift motor room**			
59	Seal off windows in LMR			
60	Seal off unnecessary opening at LMR			
61	Installation of inlet air grille and exhaust fan			
62	Installation of lighting, wiring, socket out and DB			
63	Epoxy paint of LMR floor			
64	Handover			

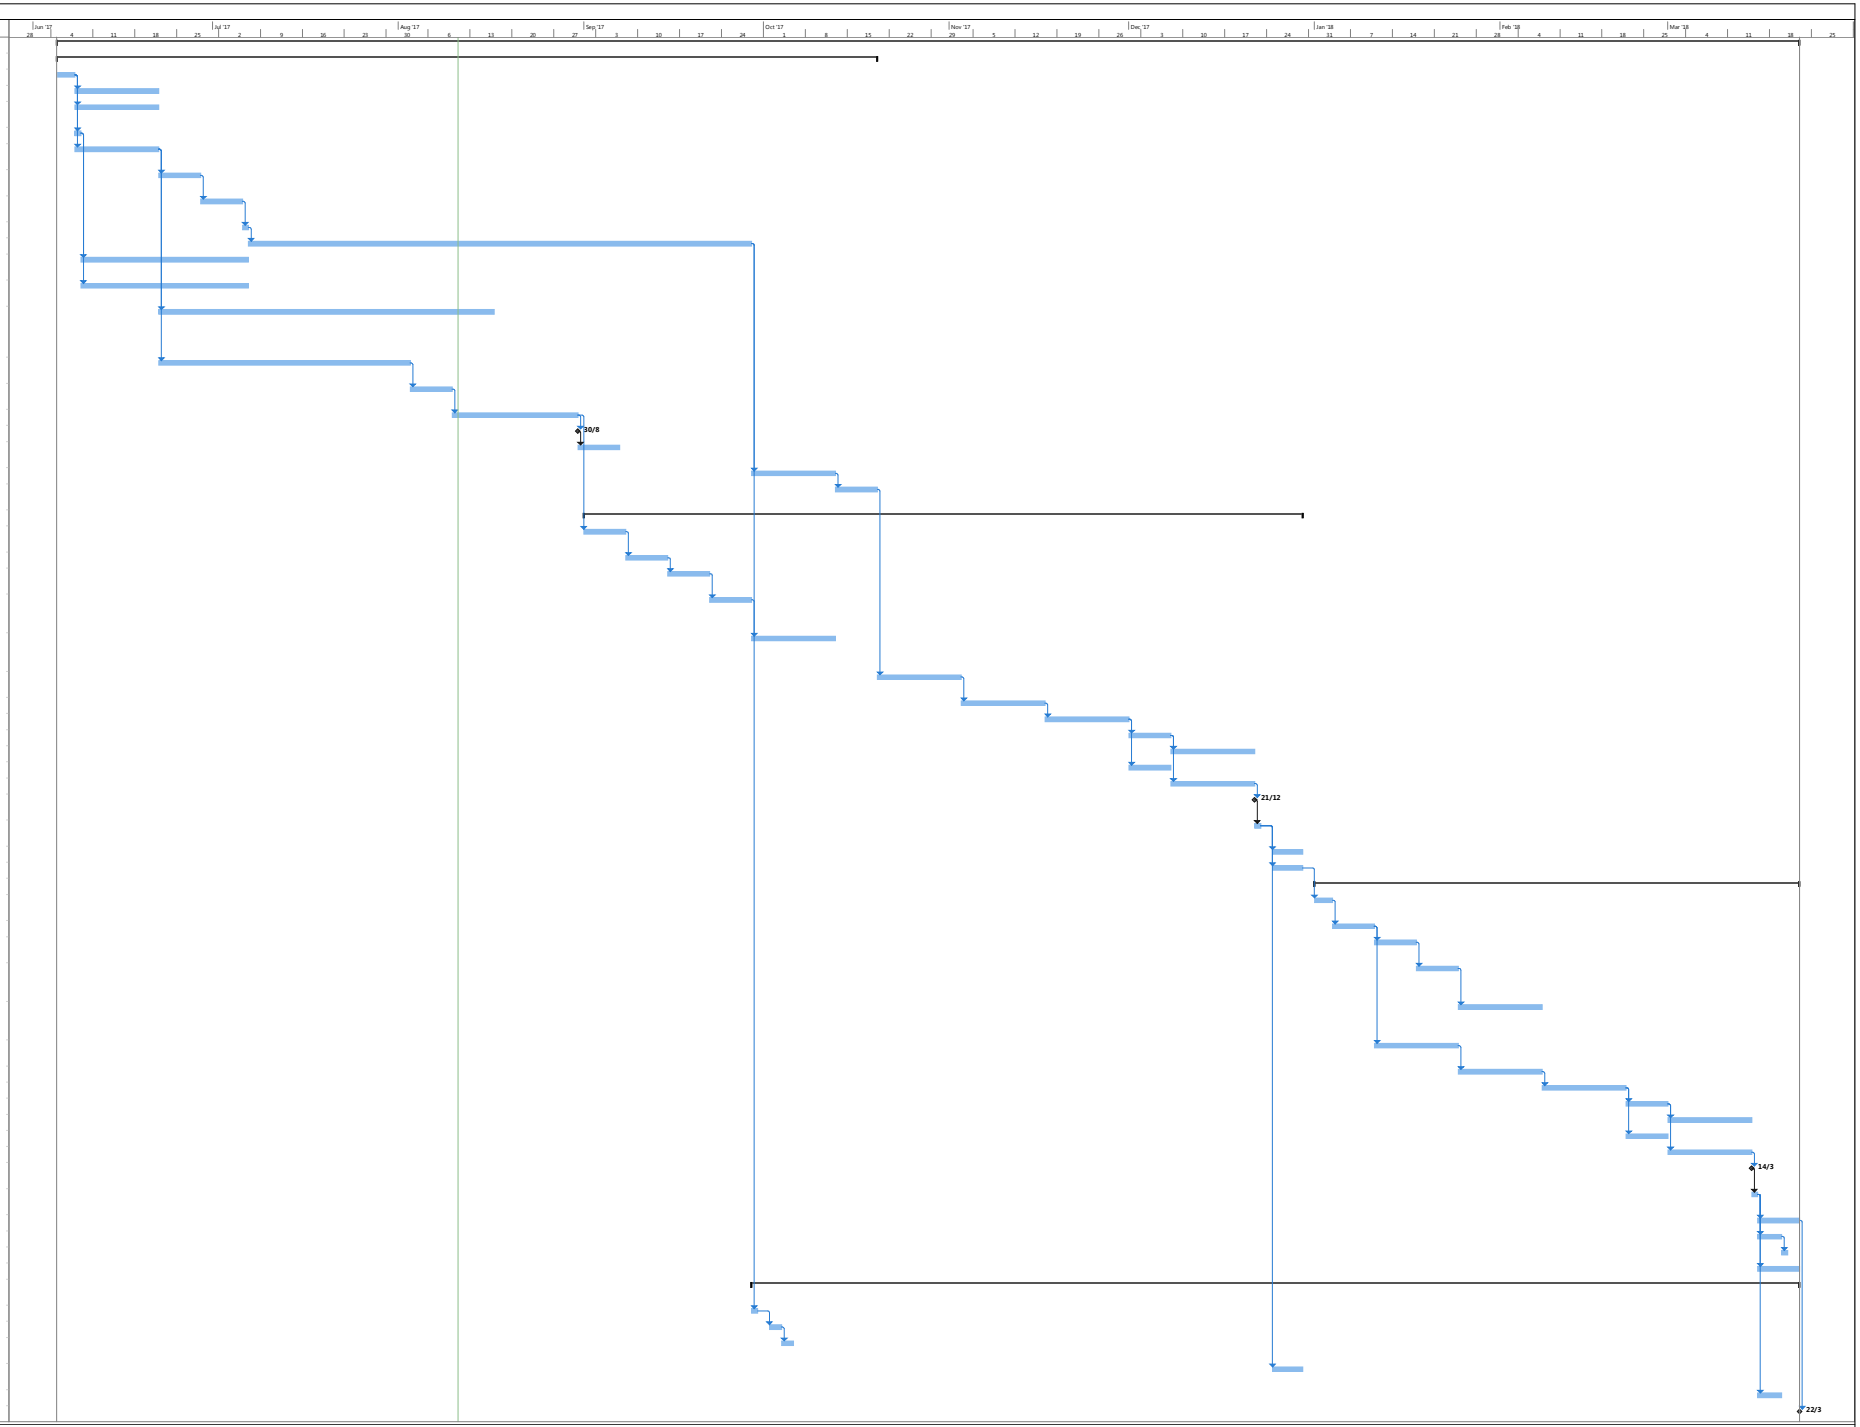

Task | Split | Milestone | Summary | Project Summary | Inactive Task | Inactive Milestone | Inactive Summary | Manual Task | Duration-only | Manual Summary Rollup | Manual Summary | Start-only | Finish-only | External Tasks | External Milestone | Deadline | Progress | Manual Progress

ANTAH BUMIMEDIC SDN. BHD.
